

June 13, 2022

## Owner Representative - Field Observation Report

The purpose of this field report is to document the project progress and the general conformance with the construction documents. The Owner's Representative has not been hired to provide safety inspection services or to guarantee that the work performed is in full compliance with the contract documents. The General Contractor/Construction Manager at Risk shall be wholly responsible for project safety, and as such, must have all procedures in place to protect workers and the public.

### Pleasant Local Schools

1107 Owens Rd W, Marion, OH 43302

Project: 219066.00 - **Pleasant Local Schools - New 5-12 Building**

Date: Tuesday, June 14, 2022 Time: 9:00 AM

Weather: Clear skies and some haze. Temp: 73 deg F Wind: 13 MPH

Contactors Present at Site: Peterson, Slagle Mechanical, Vaughn Industries, Vulcan FP, Securcom, Earthwork Construction.

- Earthworm Construction has started paving of the NW parking lot with the installation of the base course of asphalt.
- Installation of epoxy flooring in Area F is progressing on the north half.
- Installation of storefront systems continues.
- Painting in the front entry and Reception is progressing.
- Flooring installation in Areas C & D continues with the installation of stair treads and risers.
- Mechanical, fire protection, and electrical trades continue with installation of air diffusers, sprinkler heads, light fixtures and electrical devices in ceilings as grid work is completed.
- Installation of data wiring and connections continues.
- Installation of electrical circuits continues in the Kitchen.




Heavy rains overnight caused ponding, but is not affecting the paving on the west side.




Epoxy flooring installation is progressing in the Area F Performing Arts Center.



The Gym looks fantastic!

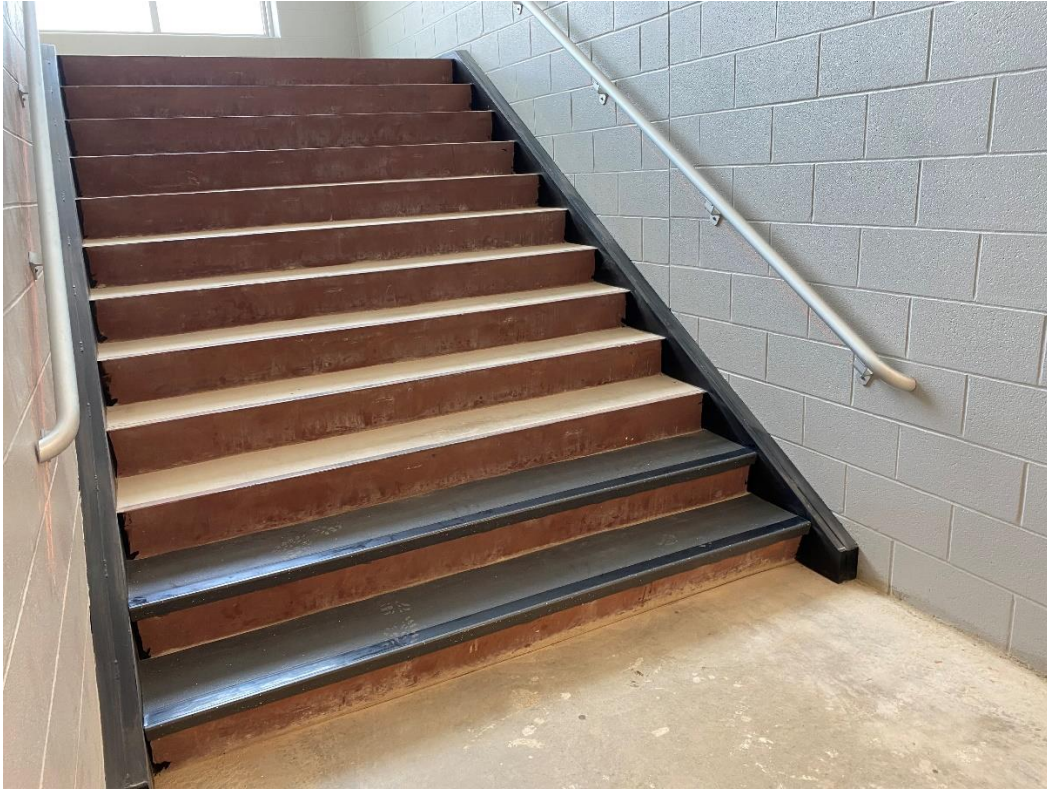

Stair treads are being "dry fitted" before permanent installation.

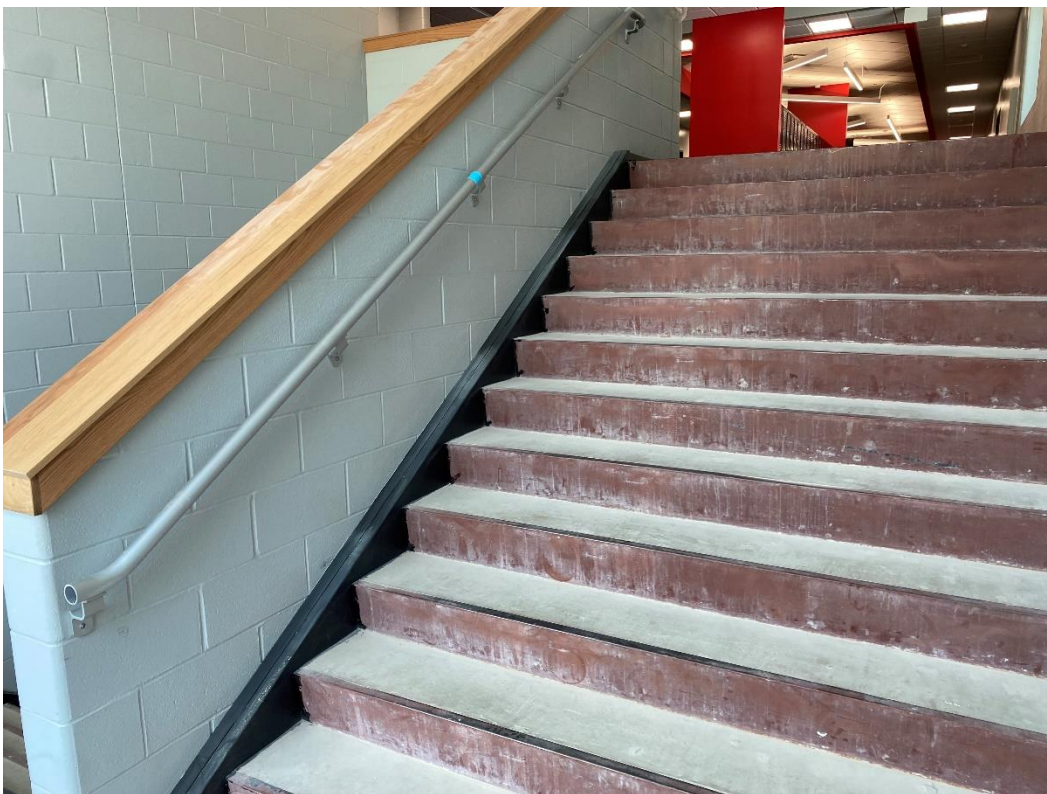

Stair handrails are being installed.



View from stage at the Performing Arts Center.



Asphalt paving work is progressing on the west side with installation of the base course.

## Next Week:

- Continue paving work.
- Continue interior painting and ceiling work.
- Continue epoxy flooring in Areas E & F.
- Start installation of wood floor at stage.
- Install exterior soffit at entry canopies.
- Install flooring in Areas A & B.
- Start installation of wood doors in C & D.
- Continue installation of wood panels in the Performing Arts Center.
- Install final ceiling systems and tiles in Areas A & B.
- Plumbing fixture, HVAC diffuser, and electrical fixture and device installation will continue.
- Continue installation of fire alarm devices, plan for test of system by weeks end.
- Install permanent lighting in mechanical rooms.
- Install exterior wall pack lighting.

END
